FINAL PROJECT REPORT

IELTS ONLINE LEARNING PLATFORM

Institution:	Ajou University in Tashkent	**Course:**	IT Project Management
Team Name:	SOLO Team	**Team Leader:**	Ra'no Botirova
Group:	I24B	**Student ID:**	202490090
Project Type:	Online Learning Platform	**Report Date:**	October 22, 2026

TABLE OF CONTENTS

1. Executive Summary
2. Introduction
3. Project Background & Problem Statement
4. Project Objectives
5. Project Scope
6. Stakeholder Analysis
7. Functional & Non-Functional Requirements
8. System Users & Use Case Analysis
9. Business Process Model (BPM)
10. Work Breakdown Structure (WBS)
11. Project Schedule & Gantt Chart
12. Project Deliverables
13. Risk Analysis
14. Project Roles & Responsibilities
15. Assumptions & Constraints
16. Expected Outcomes & Acceptance Criteria
17. Conclusion
18. References
19. Appendix

1. EXECUTIVE SUMMARY

The IELTS Online Learning Platform is an information technology project designed to support students who are preparing for the International English Language Testing System (IELTS) examination. The platform aims to bring IELTS learning materials, practice activities, progress tracking, and teacher feedback into one online system.

The project focuses on the four IELTS skills: Listening, Reading, Writing, and Speaking. Students will be able to register, log in, browse available courses, purchase access to learning materials, complete practice activities, submit written responses and speaking recordings, and review their results through a personal dashboard.

The system will also support teachers and administrators. Teachers will be able to review Writing and Speaking submissions, provide scores, and give feedback. Administrators will manage users, courses, learning materials, and payment records. A payment provider will process transactions, while the platform will verify payment status before granting access to paid content.

The project is being managed by SOLO Team for the customer, Jakhongir Isomiddinov. The project management work includes defining requirements, identifying system users, modeling business processes, preparing a Work Breakdown Structure, creating a project schedule, and preparing final documentation.

The expected result is a clear system design and project documentation package that explains how the platform should operate, what functions it should provide, and how the project activities are organized. The implementation and testing status of the software must be confirmed separately.

2. INTRODUCTION

2.1 Project Overview

Online education has become an important way for students to develop their knowledge and prepare for international examinations. IELTS candidates need regular practice, clear explanations, feedback on their performance, and an organized way to monitor their progress.

The IELTS Online Learning Platform is proposed as a centralized system for IELTS preparation. Instead of using separate tools for practice materials, written assignments, speaking recordings, and feedback, students will be able to access these activities through one platform.

The project combines IT system planning with the analysis of user requirements and business processes. It includes project planning, system modeling, scheduling, and the preparation of final project documentation.

2.2 Purpose of the Report

The purpose of this report is to present the planning and analysis work completed for the IELTS Online Learning Platform project. It describes the project objectives, scope, requirements, stakeholders, business process, work structure, schedule, risks, and expected outcomes. The report also explains how the different project management documents support the development of a clear and organized solution.

2.3 Project Team and Customer

- **Project team:** SOLO Team
- **Customer:** Jakhongir Isomiddinov
- **Project:** IELTS Online Learning Platform
- **Subject:** IT Project Management
- **Project start date:** [Insert agreed start date]
- **Project end date:** [Insert agreed completion date]

3. PROJECT BACKGROUND AND PROBLEM STATEMENT

3.1 Background

Preparing for IELTS requires students to develop four different language skills. Listening and Reading practice can often be checked automatically, while Writing and Speaking require more detailed evaluation and feedback.

When students use separate websites, documents, and communication channels for these activities, it may be difficult to keep their learning materials, results, and teacher feedback organized. Teachers may also need a structured way to receive submissions and track which assignments have been reviewed.

The project proposes an online platform that combines these activities in one system. It builds on the idea of an existing IELTS course website and plans to extend the learning experience with additional skills, payment functionality, a student dashboard, teacher review tools, and an administrator panel.

3.2 Problem Statement

The main problem addressed by this project is the lack of a single, organized learning environment that brings IELTS practice and teacher-supported assessment together. The proposed platform aims to address the following challenges:

- Students need convenient access to IELTS learning materials.
- Students need to practice Listening and Reading and review their results.
- Writing and Speaking submissions require teacher assessment and feedback.
- Students need a place to view their progress, results, and feedback.
- Administrators need tools to manage users, courses, materials, and payment records.
- Paid course access must be connected to verified payment status.

3.3 Proposed Solution

The proposed solution is a web-based IELTS learning platform with separate functions for students, teachers, administrators, and the external payment provider. Students will use the platform to study and practice. Teachers will assess submitted Writing and Speaking tasks. Administrators will manage the platform's main content and records. The payment provider will process transactions and return payment status information. This structure is intended to make IELTS preparation more convenient, organized, and manageable for both learners and staff.

4. PROJECT OBJECTIVES

4.2 Specific Objectives

1. Define the needs of students, teachers, administrators, and the customer.
2. Identify the main functional and non-functional requirements.
3. Design the system's main use cases and user interactions.
4. Model the main business process, including registration, payment, learning, submission, and assessment.
5. Organize project tasks using a Work Breakdown Structure.
6. Prepare a Gantt chart to show the project schedule.
7. Define the expected project deliverables and acceptance criteria.
8. Identify possible risks, assumptions, and project constraints.
9. Prepare clear final documentation for the customer and academic assessment.

4.3 Project Success

The project will be considered successful when the required planning documents are completed, the proposed system scope is clearly defined, and the deliverables meet the agreed requirements. If software implementation is part of the final submission, its completion and testing should also be documented using actual evidence.

5. PROJECT SCOPE

5.1 In-Scope Features

The following features are included in the planned platform scope:

- **A. Student Account Management:** Student registration; login and logout; access to personal account.
- **B. Course Access and Payment:** Browsing courses and materials; selecting course for purchase; sending payment request to external provider; checking result; granting paid access only after successful verification.
- **C. IELTS Listening and Reading:** Accessing practice activities; completing practice questions; receiving automatically calculated results where supported; viewing results.
- **D. IELTS Writing and Speaking:** Submitting Writing responses; uploading/submitting Speaking audio; allowing teachers to review submissions; providing scores and feedback; viewing feedback.
- **E. Student Dashboard:** Viewing courses and access; reviewing practice results; viewing Writing/Speaking feedback; monitoring progress.
- **F. Teacher Functions:** Viewing assigned submissions; reviewing Writing; listening to Speaking; providing scores and written feedback; updating assessment status.
- **G. Administrator Functions:** Managing user accounts, courses, learning materials, and payment records.

5.2 Out-of-Scope Items

Unless the customer approves them as additional requirements, the following are outside scope:

- A native Android or iOS application.
- Live video lessons and real-time virtual classrooms.
- Automated AI-based scoring of Writing and Speaking.
- Direct storage of students' bank card details by the platform.
- Guaranteed IELTS score improvements.
- Integration with every available payment provider.
- Features not included in the agreed requirements.

5.3 Scope Management

Any significant change to planned functions, timeline, or deliverables should be discussed with the customer before inclusion. Approved changes should be recorded so the team can assess their effect on time, effort, and quality.

6. STAKEHOLDER ANALYSIS

Stakeholders are individuals or organizations that use, support, manage, or are affected by the project.

Stakeholder	Main interest	Main responsibilities
Customer	A useful and organized IELTS learning platform	Explain needs, review deliverables, provide feedback, and approve agreed outputs
Students	Convenient IELTS preparation and clear feedback	Register, access courses, complete practice, and submit assignments
Teachers	An organized assessment process	Review Writing and Speaking submissions and provide feedback

6.1 Stakeholder Importance

The customer is important because the project requirements and final deliverables must meet their expectations. Students and teachers are the main users whose needs influence the platform's functions. Administrators support the operation of the system, while the payment provider enables paid course access.

SOLO Team is responsible for organizing the project work and preparing the documentation needed to communicate the proposed solution.

7. FUNCTIONAL AND NON-FUNCTIONAL REQUIREMENTS

7.1 Functional Requirements

Functional requirements describe what the platform should do.

ID	Requirement	Description
FR-01	Registration	The system shall allow students to create an account.
FR-02	Login	The system shall allow registered users to log in.
FR-03	Browse courses	Students shall be able to view available courses and learning materials.
FR-04	Purchase course	Students shall be able to initiate payment for a course.
FR-05	Verify payment	The platform shall verify payment status before granting paid access.
FR-06	Listening practice	Students shall be able to complete Listening activities.
FR-07	Reading practice	Students shall be able to complete Reading activities.
FR-08	View results	Students shall be able to view available practice results.
FR-09	Submit Writing	Students shall be able to submit written responses for assessment.
FR-10	Submit Speaking	Students shall be able to upload or submit Speaking recordings.
FR-11	Assess submissions	Teachers shall be able to review Writing and Speaking submissions.
FR-12	Provide feedback	Teachers shall be able to provide scores and feedback.
FR-13	Student dashboard	Students shall be able to view their available results, progress, and feedback.
FR-14	Manage users	Administrators shall be able to manage user accounts.
FR-15	Manage courses	Administrators shall be able to manage courses and learning materials.
FR-16	Manage payment records	Administrators shall be able to view and manage payment records.

7.2 Non-Functional Requirements

Non-functional requirements describe the expected quality and operational characteristics of the system:

- **Usability:** The interface should be simple enough for students and teachers to use without unnecessary difficulty.
- **Security:** User accounts and personal information should be protected through appropriate access controls.
- **Payment security:** Payment details should be handled by the payment provider. The platform should not directly store bank card details.
- **Reliability:** The system should handle common user activities consistently and display clear messages when an operation fails.
- **Performance:** Pages and learning activities should load within a reasonable time under the expected workload.
- **Maintainability:** The system should be organized so that courses, materials, and functions can be updated.
- **Compatibility:** The web platform should work with commonly used modern browsers and different screen sizes.
- **Data integrity:** User submissions, assessment results, and payment statuses should be stored and associated with the correct records.

These requirements represent the intended quality goals. Specific performance targets and security standards should be agreed with the customer if formal implementation and testing are required.

8. SYSTEM USERS AND USE CASE ANALYSIS

8.1 Overview

The Use Case Diagram identifies the main users of the IELTS Online Learning Platform and the actions each user can perform. It helps define the system boundary and clarifies how different users interact with the platform. The proposed system has four main actors: Student, Teacher, Administrator, and Payment Provider.

8.2 Student Use Cases

Students will be able to: register/login, browse courses, purchase courses, practice Listening/Reading, view practice results, submit Writing, upload Speaking recordings, view dashboard, and review scores/feedback. Access to paid course materials depends on successful payment verification.

8.3 Teacher Use Cases

Teachers will be able to: access system using account, view student submissions, review Writing, listen to Speaking, assign scores, provide written feedback, and update submission assessment information.

8.4 Administrator Use Cases

Administrators will be able to: manage user accounts, add/update/remove courses and materials, view payment records, and maintain core content.

8.5 Payment Provider Use Cases

The payment provider processes requests and returns transaction status. Unconfirmed payments will not grant access.

8.6 Use Case Summary

Actor	Main use cases
Student	Register, log in, browse courses, purchase courses, practice skills, submit assignments, view results
Teacher	Review submissions, provide scores, give feedback
Administrator	Manage users, courses, materials, and payment records
Payment Provider	Process payments and return transaction status

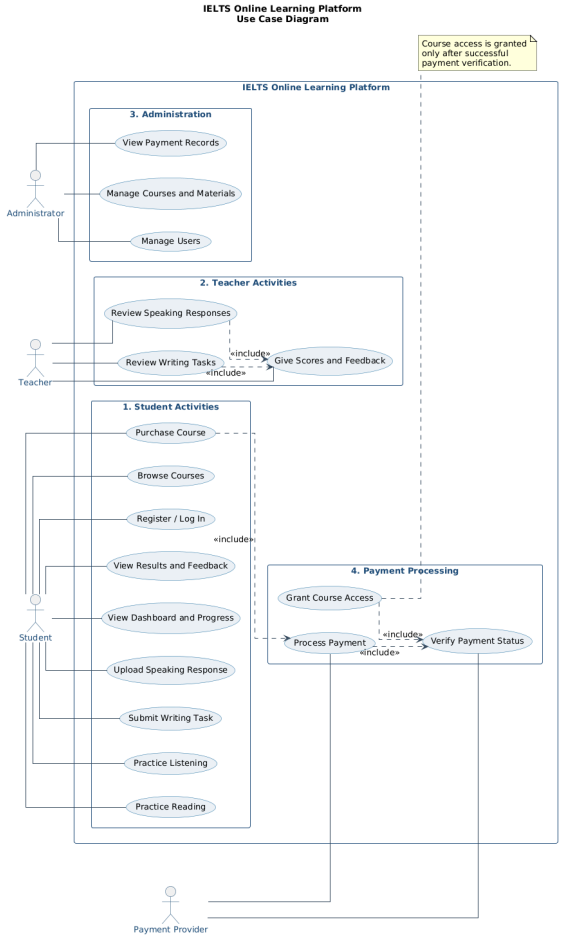


Figure 1. Use Case Diagram of the IELTS Online Learning Platform

9. BUSINESS PROCESS MODEL (BPM)

9.1 Purpose of the BPM

The Business Process Model describes how a student moves through the platform, from account registration to course access and IELTS practice. It also shows how payment processing and teacher assessment fit into the overall process. The BPM is useful because it explains the sequence of activities and decisions, rather than only listing the system's functions.

9.2 Main Business Process

Stage 1: Registration and Login — Student opens platform and registers/logs in. Correct auth enables course browsing.
Stage 2: Course Selection and Payment — Student selects course, sends payment request. Provider processes status. Failed payments prompt retry/cancel; verified payments grant access.
Stage 3: Learning and Practice — Student selects activity. Listening/Reading practice auto-scores. Writing/Speaking sends submissions to teacher review.
Stage 4: Teacher Assessment — Teacher opens work, reviews, assigns score, and submits feedback.
Stage 5: Dashboard and Progress Review — Student views results and feedback via personal dashboard.

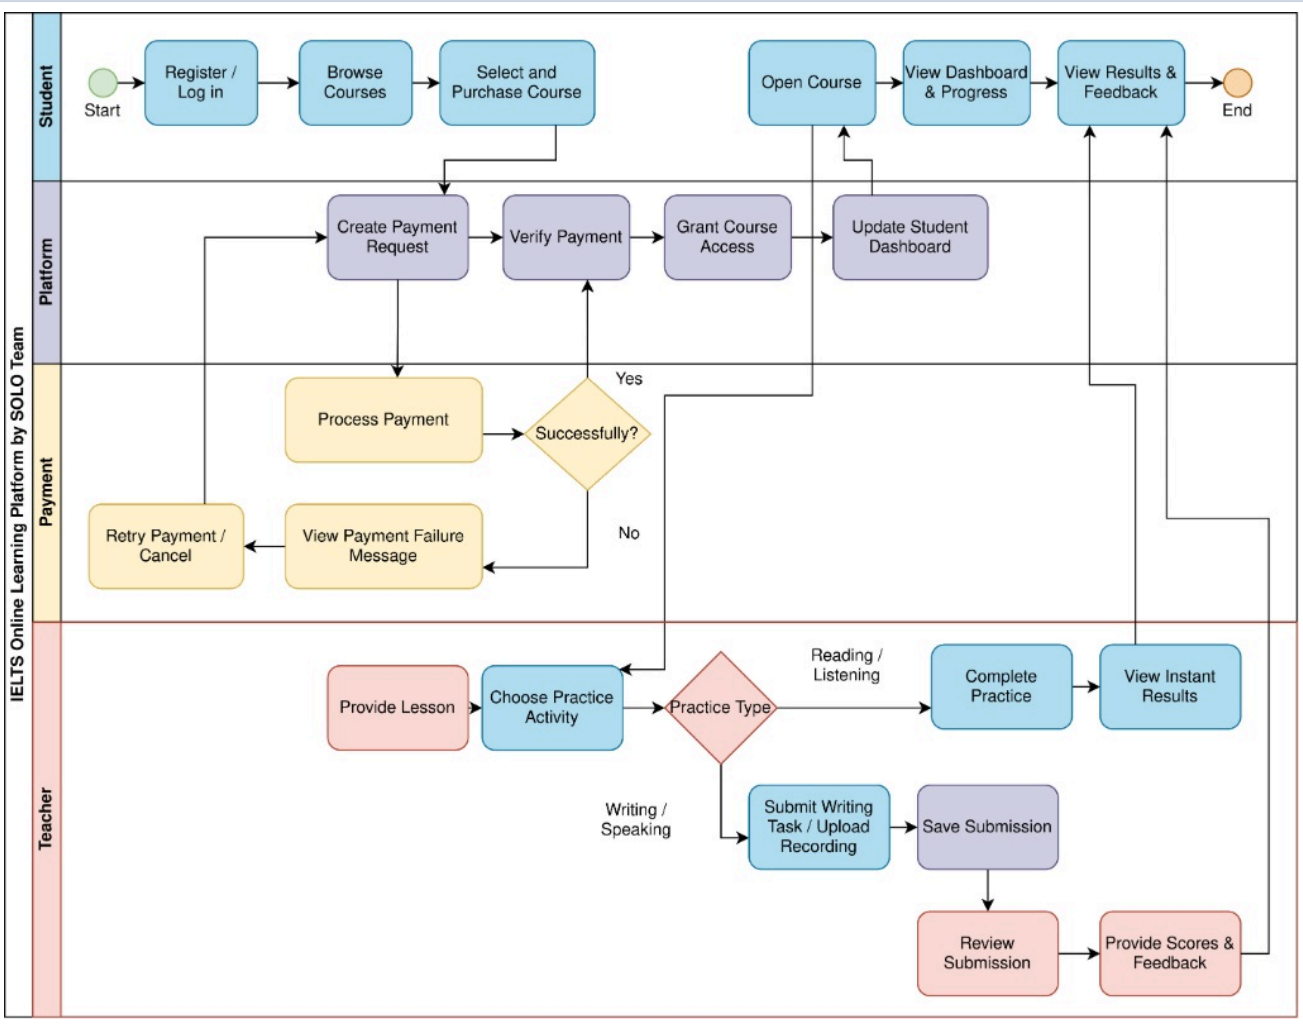


Figure 2. Business Process Model (BPM) Swimlane Diagram

9.4 BPM Benefits

The BPM clarifies the relationship between student activities and system operations. It highlights important decision points, particularly payment verification and the distinction between automatically scored practice and teacher-reviewed submissions.

10. WORK BREAKDOWN STRUCTURE (WBS)

10.1 Purpose of the WBS

The Work Breakdown Structure divides the project into smaller, manageable tasks. It helps the team organize responsibilities, estimate the required effort, track progress, and ensure that the important project activities are not overlooked. The WBS for this project is organized into six main work packages.


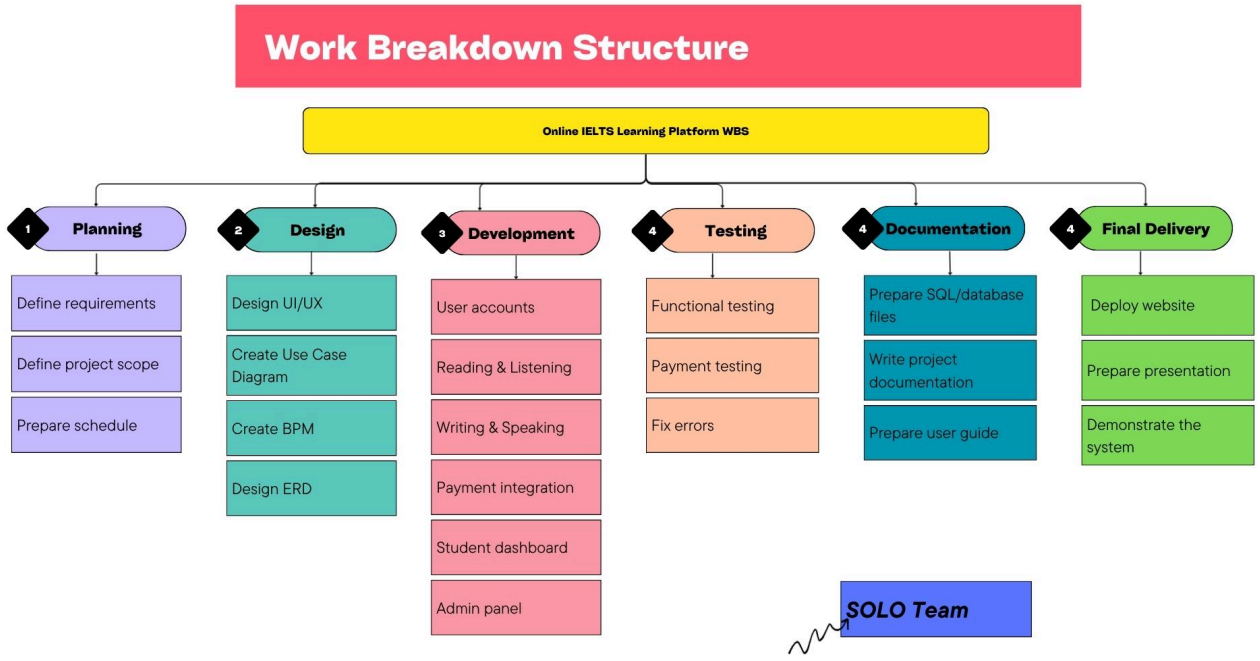


Figure 3. Work Breakdown Structure (WBS) Diagram

11. PROJECT SCHEDULE AND GANTT CHART

11.1 Purpose of the Schedule

The Gantt chart presents the planned timeline for the project. It shows when the main activities are scheduled and helps the team coordinate the completion of project documents and the final presentation. The schedule provided for the project covers the period from late September to October 2026.

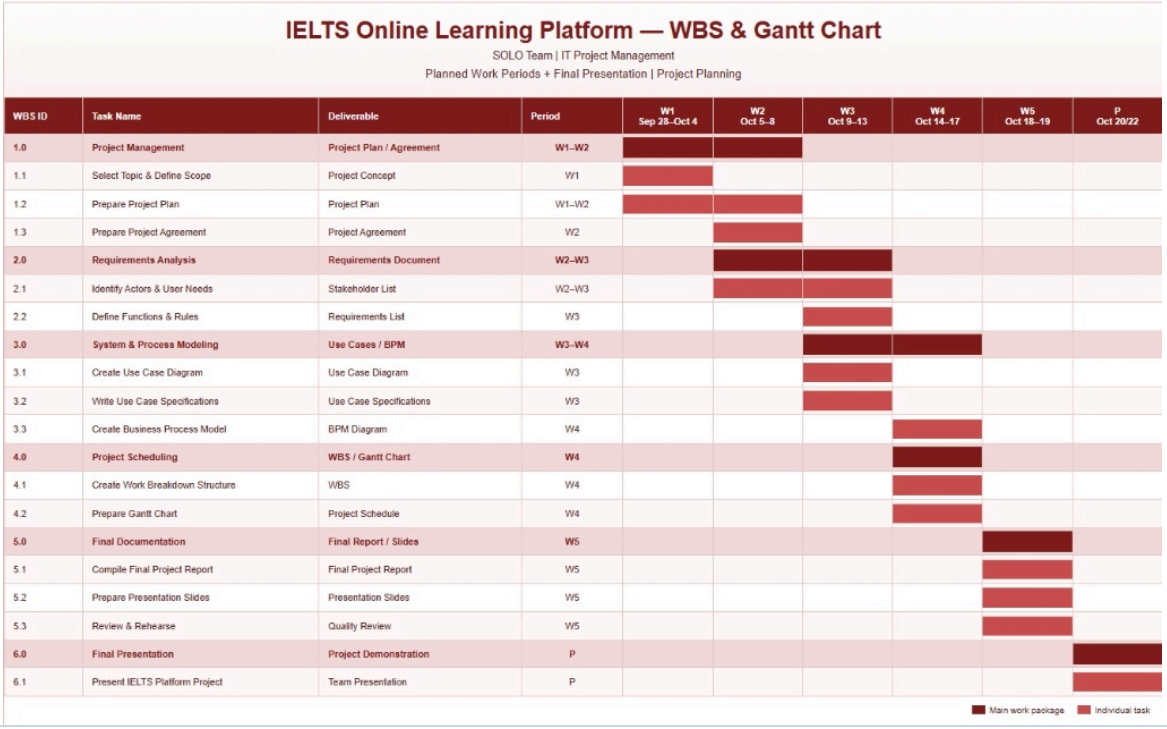

12. PROJECT DELIVERABLES

No.	Deliverable	Purpose
1	Project Plan	Defines project goals & activities.
2	Project Agreement	Documents purpose, scope, responsibilities.
3	Requirements Analysis	Describes user needs & platform functions.
4	Use Case Diagram	Shows actors & system interactions.
5	BPM Diagram	Describes workflow for payment & learning.
6	WBS Diagram	Divides project into manageable tasks.
7	Gantt Chart	Shows schedule & planned activity dates.
8	Final Project Report	Combines analysis & planning into report.
9	Presentation Slides	Summarize project for final presentation.

13. RISK ANALYSIS

ID	Risk	Prob/Imp	Mitigation
R1	Unclear requirements	Med / High	Confirm requirements with customer.
R2	Tasks delayed	Med / High	Monitor Gantt chart priorities.
R3	Inconsistent diagrams	Med / Med	Cross-check WBS/BPM/Use Cases.
R4	Payment verification error	Med / High	Verify status before access.
R5	Unauthorized access	Med / High	Apply role authentication.
R6	Data/Submission loss	Low / High	Use relational DB & backups.
R7	Report incomplete	Med / High	Reserve review time before submission.

14. ROLES & RESPONSIBILITIES

Role	Assigned Person
Project Coordinator	Ra'no Botirova
Requirements Analyst	SOLO Team Member
System/Process Modeler	SOLO Team Member
Project Planner	SOLO Team Member
Documentation Coordinator	SOLO Team Member
Customer	Jakhongir Isomiddinov

15. ASSUMPTIONS & CONSTRAINTS

Assumptions: Internet & browser access available; distinct role permissions enforced; payment gateway confirms status; teachers grade Writing/Speaking; Reading/Listening auto-scores.
Constraints: Timeframe limits; skill/resource boundary; course requirements; external payment API dependence.

16. EXPECTED OUTCOMES & ACCEPTANCE

The platform provides an organized IELTS learning environment. Acceptance criteria (AC-01 to AC-09) verify purpose, scope, user roles, workflows, WBS, schedule, risk mitigation, and document consistency.

17. CONCLUSION

The project demonstrates IT project management methodologies applied to an online learning system. The documentation establishes a solid foundation for future software implementation.

18. REFERENCES & 19. APPENDIX

1. SOLO Team. IELTS Online Learning Platform Project Agreement. Project document, October 22, 2026.
2. SOLO Team. IELTS Online Learning Platform — Use Case Diagram. Project diagram.
3. SOLO Team. IELTS Online Learning Platform — Business Process Model. Project diagram.
4. SOLO Team. IELTS Online Learning Platform — Work Breakdown Structure. Project planning diagram.
5. SOLO Team. IELTS Online Learning Platform — Gantt Chart. Project schedule.
6. ITPM Mid-Term Project Repository: https://github.com/rbtrv/ITPM_Mid-Term_Project
